

NEW lateral

FOLLOWING DATA TO BE ANSWERED BY INSPECTOR
AND SIGNED WHEN RETURNED

No. 4324

DATE INSPECTED 5-12-42

IF SO HOW AND LOCATION FROM
FIRST MANHOLE DOWN STREAM

59' out in Street

HOUSE NO. 334

DISTANCE FROM FIRST MANHOLE
DOWN STREAM TO DITCH AT
CURB LINE AND DEPTH

SIZE OF PIPE USED 6"

WAS LATERAL AT CURB?

yes

NAME OF CONTRACTOR

Geo. Farley

WAS ATTACHED TO MAIN


SHOW BY DIAGRAM RELATION OF LATERAL TO WALL OF BUILDING SERVED.

Lateral 7.5' Deep at curb

Lateral 4' Deep at House

Lateral 41' Long House to curb

Res.

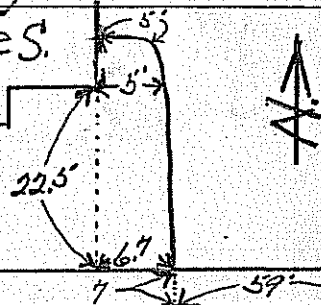

curb

Sewer

Highland Ave SE

SIGNED

Julius M. Olson
INSPECTOR FOR CITY

FILED AT ENGINEER'S OFFICE

oic GCW
May 13 1942

REMARKS

+ mark on top of curb "Soil Clay & Gravel"

No. 4324

PERMIT TO TAP SEWER

DATE OF PERMIT 5/7

MASSILLON, OHIO

15

RECEIVED OF

FEE OF \$

FOR WHICH PERMISSION IS GRANTED

TO TAP

SEWER, ON THE

OF

AVE., TYPE OF STREET
ST.,

THE PREMISES BEING LOT No.

HOUSE No.

WORK TO BE DONE IN ACCORDANCE WITH ORDINANCE No. 2323, DULY PASSED BY THE CITY COUNCIL
RULES OF THE DEPARTMENT OF PUBLIC SERVICE.

NAME OF CONTRACTOR

Note. This permit covers work outside of building only. Any work inside
of building is subject to Massillon Board of Health Regulations.
