

Nº 4494

FOLLOWING DATA TO BE ANSWERED BY INSPECTOR
AND SIGNED WHEN RETURNED

DATE INSPECTED 8-22-44

IF SO HOW AND LOCATION FROM
FIRST MANHOLE DOWN STREAM

See sketch

HOUSE NO. 455

SIZE OF PIPE USED 6"

DISTANCE FROM FIRST MANHOLE
DOWN STREAM TO DITCH AT
CURB LINE AND DEPTH


See sketch

WAS LATERAL AT CURB? No.

WAS ATTACHED TO MAIN Tapped Main

NAME OF CONTRACTOR Del. Earley

SHOW BY DIAGRAM RELATION OF LATERAL TO WALL OF BUILDING SERVED.

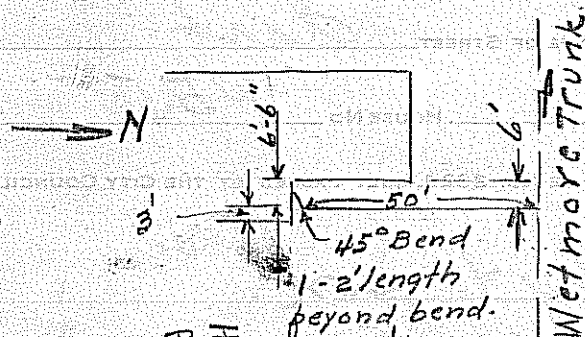

Tapped main line
4'-6" Deep at main
2'-0" Deep at house
Length 50' from main to
45° Bend at house. One 2' l.
Laid beyond bend. No manhole
located on main line.

SIGNED R. F. Snyder
INSPECTOR FOR CITY

FILED AT ENGINEER'S OFFICE

REMARKS: Sandy soil. No location or indication of curb line or prop. line for further location.

OFFICE OF THE DIRECTOR OF PUBLIC SERVICE

N^o 4494

PERMIT TO TAP SEWER

MASSILLON, OHIO, 8/17

RECEIVED OF

FEE OF \$2

FOR WHICH PERMISSION IS GRANTED

TO TAP

SEWER, ON THE

OF

AVE., TYPE OF STREET

ST.,

THE PREMISES BEING LOT NO.

HOUSE NO.

WORK TO BE DONE IN ACCORDANCE WITH ORDINANCE NO. 2323, DULY PASSED BY THE CITY COUNCIL
 RULES OF THE DEPARTMENT OF PUBLIC SERVICE.

NAME OF CONTRACTOR

Note. This permit covers work outside of building only. Any work
 walls of building is subject to Massillon Board of Health Regulations.
