



C&K Industrial Services, Inc.
5617 E. Schaaf Rd.
Independence, Ohio 44131
216-642-0055

PACP Report with Pipe Run and Incident Snapshots

Surveyed by: Mike Head	Certificate number: 123456	Owner: C & K Industrial Service, Inc	Customer:	Drainage area:	P/O number:	Sheet number:
Pipe segment ref.: SNG-4-13	Start date/time: 20220915 09:56	Street: ERIE ST	City: MASSILLON			
Location details:		Upstream MH No: 1103 MAIN TRUNK	Rim to invert:	Grade to invert:	Rim to grade:	
Pipe use: SS	Direction: D	Flow control:	Downstream MH No: 1288 SR21	Rim to invert:	Grade to invert:	Rim to grade:
Height: 78 in.	Width:	Shape: C	Material: RCP	Lining method:	Pipe joint length:	Total length: 544.200 ft.
Length surveyed: 544.200 ft.	Purpose:	Sewer category:				
Media label:	Pre-cleaning: N	Date cleaned:	Weather: 1	Location code:	Pressure value:	
Project name: CITY OF MASSILLON	Additional info:					


Grade	Structural:					O&M:					Overall:	
	Amount of Defects	Segment Grade	Pipe Rating	Quick Rating	Pipe Rating Index	Amount of Defects	Segment Grade	Pipe Rating	Quick Rating	Pipe Rating Index	Pipe Rating	Pipe Rating Index
1	0	0	0	0000	0.0	0	0	222	2U00	2.0	222	2.0
2	0	0				111	222					
3	0	0				0	0					
4	0	0				0	0					
5	0	0				0	0					

Observations


Distance	Video Ref.	PACP Code	Continuous	S/M/L	Value Inches (mm) 1st 2nd	%	Joint	Circumferential Location At/From To	Rating	Image Ref.	Remarks
0.0 ft.		AMH					☐	/		CITY OF MASSILLON-AMH '1103 MAIN TRUNK'-AMH '1288 SR21'-AMH at 0.0 ft.JPG	1103 MAIN TRUNK
0.0 ft.		MWL				20	☐	/		CITY OF MASSILLON-AMH '1103 MAIN TRUNK'-AMH '1288 SR21'-MWL at 0.0 ft.JPG	
60.9 ft.	00:05:08	DSF	S01			10	☐	5 / 7	2	CITY OF MASSILLON-AMH '1103 MAIN TRUNK'-AMH '1288 SR21'-DSF at 60.9 ft.JPG	
60.9 ft.	00:04:40	TBA			4.000		☐	10 /		CITY OF MASSILLON-AMH '1103 MAIN TRUNK'-AMH '1288 SR21'-TBA at 60.9 ft.JPG	
467.9 ft.	00:24:36	LL				20	☐	/	2	CITY OF MASSILLON-AMH '1103 MAIN TRUNK'-AMH '1288 SR21'-LL at 467.9 ft.JPG	
479.7 ft.	00:27:02	OBR	S02			10	☐	5 / 7	2	CITY OF MASSILLON-AMH '1103 MAIN TRUNK'-AMH '1288 SR21'-OBR at 479.7 ft.JPG	

Observations

Distance	Video Ref.	PACP Code	Continuous	S/M/L	Value Inches (mm)	%	Joint	Circumferential Location At/From To	Rating	Image Ref.	Remarks
					1st2nd						
482.6 ft.	00:28:20	MSC			78.000		☐	/		CITY OF MASSILLON-AMH '1103 MAIN TRUNK'-AMH '1288 SR21'-MSC at 482.6 ft.JPG	CHANGES TO A SQUARE PIPE
544.2 ft.	00:35:32	AOC					☐	/		CITY OF MASSILLON-AMH '1103 MAIN TRUNK'-AMH '1288 SR21'-AOC at 544.2 ft.JPG	1288 SR21
544.2 ft.	00:35:08	DSF	F01			10	☐	5 / 7	2	CITY OF MASSILLON-AMH '1103 MAIN TRUNK'-AMH '1288 SR21'-DSF at 544.2 ft.JPG	
544.2 ft.	00:35:17	OBR	F02			10	☐	5 / 7	2		

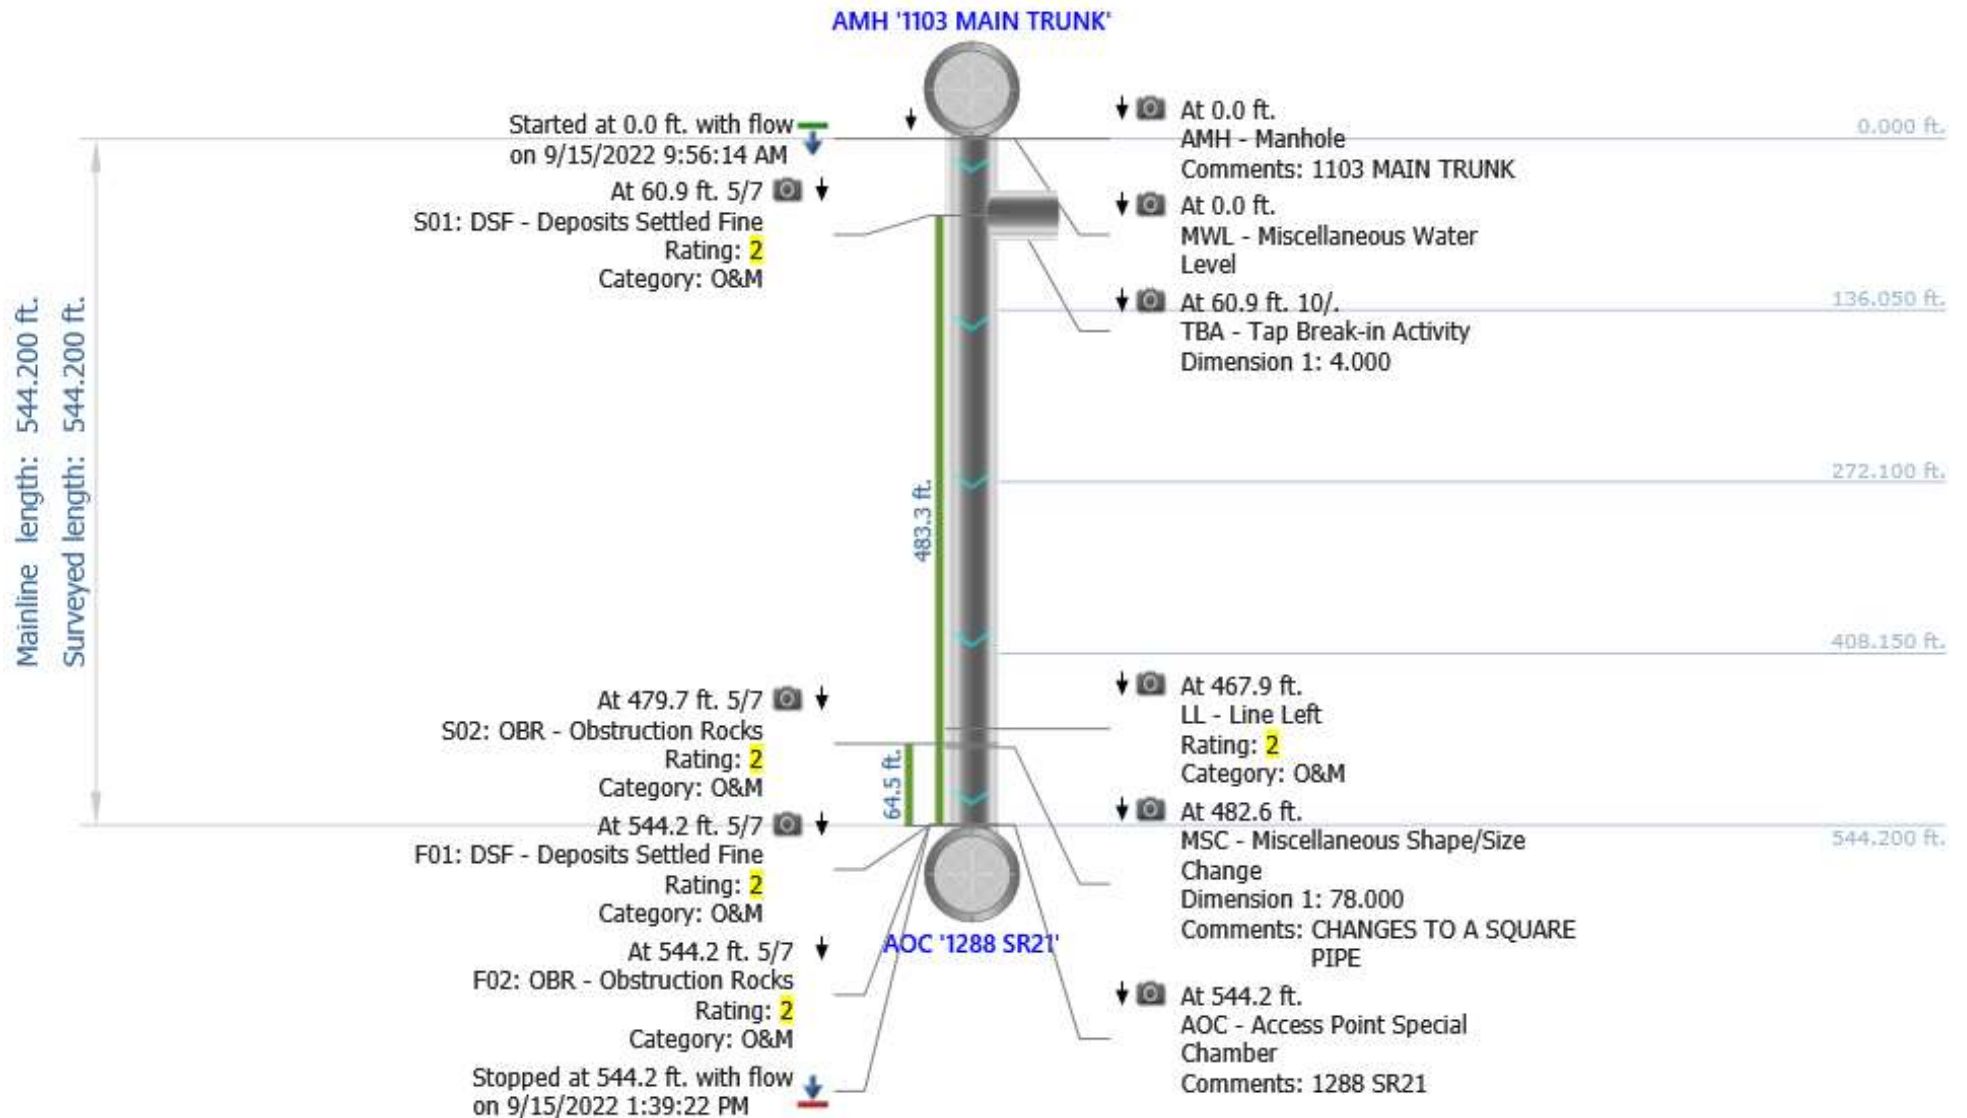

Photos

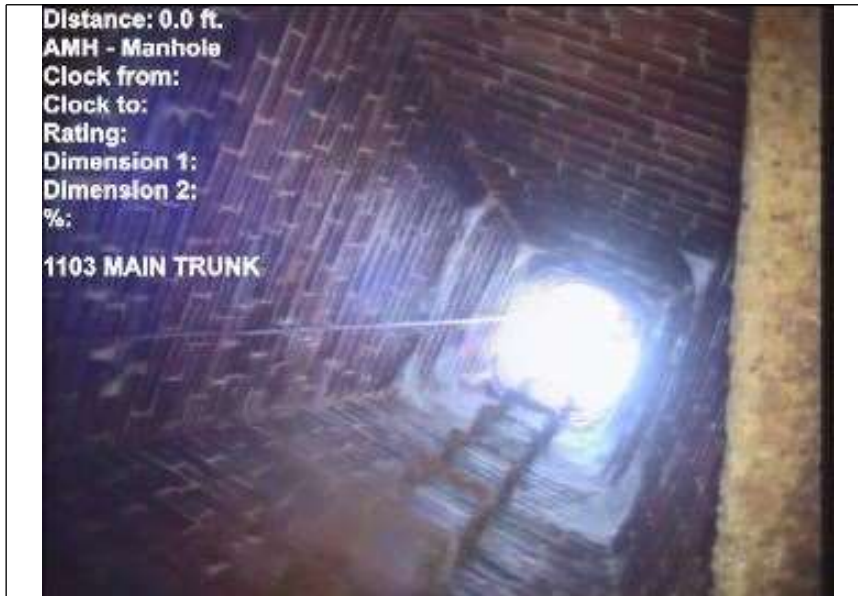

At: 0 ft. AMH - Manhole
Joint: No 1103 MAIN TRUNK



At: 0 ft. MWL - Miscellaneous Water Level
Joint: No 20 %



At: 60.9 ft. 5/7 DSF - Deposits Settled Fine
Joint: No 10 %



At: 60.9 ft. 10/ TBA - Tap Break-in Activity
Joint: No


Photos



At: 467.9 ft. LL - Line Left
Joint: No 20 %



At: 479.7 ft. 5/7 OBR - Obstruction Rocks
Joint: No 10 %

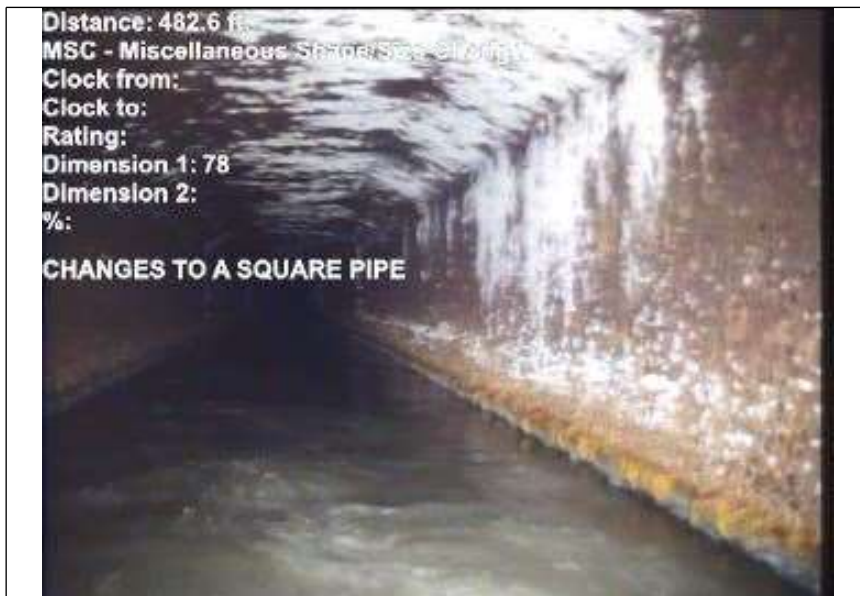

At: 482.6 ft. MSC - Miscellaneous Shape/Size Change
Joint: No CHANGES TO A SQUARE PIPE



At: 544.2 ft. AOC - Access Point Special Chamber
Joint: No 1288 SR21

Photos



At: 544.2 ft. 5/7 DSF - Deposits Settled Fine
Joint: No 10 %
